



55 Hartland Street
East Hartford, CT 06108
860.282.9924 | oneatlas.com

October 8, 2026

Mr. John Butrymovich
Facilities Director
Bolton Public Schools
72 Brandy Street
Bolton, CT 06043

Re: Asbestos Roof Inspection
Bolton Public Schools
108 Notch Road, Bolton, CT 06043
Atlas Project No. 2438026001

Dear Mr. Butrymovich:

Atlas Technical Consultants LLC (Atlas) collected bulk samples of suspect asbestos-containing materials (ACM) at the above-referenced site on September 30, 2026. The fieldwork was performed by Aaron Blanchflower and Arlene Blackwell, State of Connecticut Department of Public Health (CTDPH) licensed asbestos inspectors (CTDPH license number 001253 and 001151, respectively).

The work was performed in response to the roof replacement project. Sampling was limited to the three (3) main roof fields for the Bolton Center School, 108 Notch Road in Bolton, CT.

ASBESTOS BULK SAMPLE COLLECTION:

Building materials considered suspect ACM were inspected and assessed using the methods presented in the United States Environmental Protection Agency AHERA regulations (40 CFR Part 763) and NESHAP regulations (40 CFR Part 61).

Atlas collected bulk samples of building materials utilizing a sampling strategy that correlated with 40 CFR 763.86 as follows:

- (a) *Surfacing materials.* An accredited inspector shall collect, in a statistically random manner that is representative of the homogeneous area, bulk samples from each homogeneous area of friable surfacing material that is not assumed to be ACM, and shall collect the samples as follows:
 - (1) At least three bulk samples shall be collected from each homogeneous area that is 1,000 ft² or less, except as provided in 40 CFR Part 763.87(c)(2).
 - (2) At least five bulk samples shall be collected from each homogeneous area that is greater than 1,000 ft² but less than or equal to 5,000 ft², except as provided in 40 CFR Part 763.87(c)(2).
 - (3) At least seven bulk samples shall be collected from each homogeneous area that is greater than 5,000 ft², except as provided in 40 CFR Part 763.87(c)(2).
- (b) *Thermal system insulation.*
 - (1) Except as provided in paragraphs (b)(2) through (4) of this section and 40 CFR Part 763.87(c), an accredited inspector shall collect, in a randomly distributed manner, at least three bulk samples from each homogeneous area of thermal system insulation that is not assumed to be ACM.
 - (2) Collect at least one bulk sample from each homogeneous area of patched thermal system insulation that is not assumed to be ACM if the patched section is less than 6 linear or square feet.

- (3) In a sufficient manner to determine whether the material is ACM or not ACM, collect bulk samples from each insulated mechanical system that is not assumed to be ACM where cement or plaster is used on fittings such as tees, elbows, or valves, except as provided under 40 CFR Part 763.87(c)(2).
 - (4) Bulk samples are not required to be collected from any homogeneous area where the accredited inspector has determined that the thermal system insulation is fiberglass, foam glass, rubber, or other non-ACM.
- (c) *Miscellaneous materials.* In a manner sufficient to determine whether material is ACM or not ACM, an accredited inspector shall collect bulk samples from each homogeneous area of friable or non-friable miscellaneous material that is not assumed to be ACM.

ASBESTOS-CONTAINING MATERIALS:

Atlas Technical Consultants LLC (Atlas) collected bulk samples of suspect asbestos-containing materials (ACM) for the roof sections at the above-referenced site on September 30, 2026.

The EPA recognizes the following as asbestos: Chrysotile, Crocidolite, Amosite, Tremolite, Actinolite, and Anthophyllite. To be classified as ACM, the material must be determined to contain greater than or equal to one percent (1%) asbestos. In order to consider a material to be non-ACM, all samples of a homogeneous type of material that are collected must be analyzed and all results must indicate the material to contain less than 1% asbestos by weight. The CTDPH defines ACM as any material containing greater than or equal to 1% asbestos. The Occupational Safety and Health Administration (OSHA) regulates material containing any detectable amount of asbestos.

Atlas collected a total of seventy-one (71) bulk samples. The bulk samples collected during the survey were analyzed by EMSL Analytical, Inc. (NVLAP #200700-0) located in Meriden, Connecticut. The bulk samples were analyzed by Polarized Light Microscopy (PLM) with dispersion staining via EPA 600/R-93/116 Method. Utilizing PLM, the microscopist is able to identify and distinguish between asbestos group minerals and other fibrous materials such as cellulose, mineral wool, fiberglass, or synthetic fibers. The quantities of each of these substances is estimated based on the procedures defined in the above-cited reference and are reported as a percentage. Results are summarized in the following table, and the laboratory analysis report and associated chain-of-custody form are attached. The site sample location map is also attached to this report.

Sample Number	Location	Material	Asbestos (% Type)
093026-1A	Roof A - Core 1	Top Layer Tar and Gravel	NAD
093026-1B	Roof A - Core 1	Top Layer Tar and Gravel	NAD
093026-2A	Roof A - Core 1	Middle Layer Fibrous	NAD
093026-2B	Roof A - Core 1	Middle Layer Fibrous	NAD
093026-3A	Roof A - Core 1	Bottom Layer Foam	NAD
093026-3B	Roof A - Core 1	Bottom Layer Foam	NAD
093026-4A	Roof A - North	Stucco Wall	NAD

Sample Number	Location	Material	Asbestos (% Type)
093026-4B	Roof A - East	Stucco Wall	NAD
093026-4C	Roof A - South	Stucco Wall	NAD
093026-5A	Roof A	White Vent Caulking	NAD
093026-5B	Roof A	White Vent Caulking	NAD
093026-6A	Roof A	Black Roof Patch, at Roof Vents	8% CH
093026-6B	Roof A	Black Roof Patch, at Perimeter	NAD
093026-7A	Roof A	Silver Roof Patch	NAD
093026-7B	Roof A	Silver Roof Patch	NAD
093026-8A	Roof A	White Caulking on Flashing Tape	NAD
093026-8B	Roof A	White Caulking on Flashing Tape	NAD
093026-9A	Roof A	White Seam Caulking	NAD
093026-9B	Roof A	White Seam Caulking	NAD
093026-10A	Roof A	Cement Chimney Cap	NAD
093026-10B	Roof A	Cement Chimney Cap	NAD
093026-11A	Roof A	Shingle Edge	NAD
093026-11B	Roof A	Shingle Edge	NAD
093026-12A	Roof B	Chimney Brick	NAD
093026-12B	Roof B	Chimney Brick	NAD
093026-13A	Roof B	Chimney Mortar	NAD
093026-13B	Roof B	Chimney Mortar	NAD
093026-14A	Roof B	Edge Roof Patch	NAD
093026-14B	Roof B	Edge Roof Patch	NAD
093026-15A	Roof B	Air Conditioner Unit Patch	NAD
093026-15B	Roof B	Air Conditioner Unit Patch	NAD
093026-16A	Roof B	Skylight Shingles	NAD

Sample Number	Location	Material	Asbestos (% Type)
093026-16B	Roof B	Skylight Shingles	NAD
093026-17A	Roof B	Skylight Caulking	NAD
093026-17B	Roof B	Skylight Caulking	NAD
093026-18A	Roof B	White Flashing Tar	NAD
093026-18B	Roof B	White Flashing Tar	NAD
093026-19A	Roof B	Black Flashing Tar	NAD
093026-19B	Roof B	Black Flashing Tar	NAD
093026-20A	Roof B – Core 2	Top Layer Tar and Gravel	NAD
093026-20B	Roof B – Core 2	Top Layer Tar and Gravel	NAD
093026-21A	Roof B – Core 2	2nd Layer Fibrous	NAD
093026-21B	Roof B – Core 2	2nd Layer Fibrous	NAD
093026-22A	Roof B – Core 2	3 rd Layer Paper	NAD
093026-22B	Roof B – Core 2	3 rd Layer Paper	NAD
093026-23A	Roof B – Core 2	4 th Layer Foam	NAD
093026-23B	Roof B – Core 2	4 th Layer Foam	NAD
093026-24A	Roof B – Core 2	Bottom Layer Paper	NAD
093026-24B	Roof B – Core 2	Bottom Layer Paper	NAD
093026-25A	Roof C	Edge Roof Caulking	NAD
093026-25B	Roof C	Edge Roof Caulking	NAD
093026-26A	Roof C	Black Vent Caulking	NAD
093026-26B	Roof C	Black Vent Caulking	NAD
093026-27A	Roof C	Red Shingle	NAD
093026-27B	Roof C	Red Shingle	NAD
093026-28A	Roof C	Edge Roof Patch	NAD
093026-28B	Roof C	Edge Roof Patch	NAD

Sample Number	Location	Material	Asbestos (% Type)
093026-29A	Roof C	Shingle Seam Caulking	NAD
093026-29B	Roof C	Shingle Seam Caulking	NAD
093026-30A	Roof C – Core 3	Top Layer Tar and Gravel	NAD
093026-30B	Roof C – Core 3	Top Layer Tar and Gravel	NAD
093026-31A	Roof C – Core 3	2 nd Layer Fibrous	NAD
093026-31B	Roof C – Core 3	2 nd Layer Fibrous	NAD
093026-32A	Roof C – Core 3	3 rd Layer Paper	NAD
093026-32B	Roof C – Core 3	3 rd Layer Paper	NAD
093026-33A	Roof C – Core 3	4 th Layer Foam	NAD
093026-33B	Roof C – Core 3	4 th Layer Foam	NAD
093026-34A	Roof C – Core 3	5 th Layer Paper	NAD
093026-34B	Roof C – Core 3	5 th Layer Paper	NAD
093026-35A	Roof C – Core 3	6 th Layer (Bottom) Foam	NAD
093026-35B	Roof C – Core 3	6 th Layer (Bottom) Foam	NAD

NAD = No Asbestos Detected

CH = Chrysotile Asbestos

Laboratory analysis determined that the following roof material is an asbestos-containing material (ACM):

- Roof A (Northeast Section) Black Roof Patch at Roof Vents (approximately 25 linear feet).

All the other samples for the roof inspection were determined through laboratory analysis to be none detected for asbestos (NAD).

REGULATORY DISCUSSION:

EPA regulations require the removal of Regulated Asbestos-Containing Materials (RACM) prior to renovation or demolition activities. RACM is defined as (a) Friable ACM, (b) Category I non-friable ACM that has become friable, (c) Category I non-friable ACM that will be or has been subjected to sanding, grinding, cutting, or abrading, or (d) Category II non-friable ACM that has a high probability of becoming or has become crumbled, pulverized, or reduced to powder by the forces expected to act on the material in the course of demolition or renovation activities. The CTDPH defines "asbestos abatement" as removal, encapsulation, enclosure, renovation, repair, demolition, or other disturbance of ACM but does not include activities which are related to (A) the removal or repair of asbestos cement pipe and are performed by employees of a water company as defined in section 25-32a, or (B) the removal of non-friable ACM found exterior to a building or structure other than material defined as RACM in 40 CFR 61, the National Emission Standards for Hazardous Air Pollutants (NESHAP).

Based upon these definitions, ACM identified in the building requires removal prior to renovation, demolition, or disturbance. The State of Connecticut Department of Energy and Environmental Protection (CTDEEP) regulations require the proper disposal of all ACM, regardless of categorization.

LIMITATIONS:

As with all such assessments, the results of the sampling represent conditions found on the date of the survey and may not represent conditions found at other times. Additionally, this assessment was limited with respect to the specific parameters indicated above and should not be construed to be a comprehensive evaluation or a definitive representation of conditions within the facility. The information presented in this report is intended to be used as a guide to evaluate the need for further investigation or the need for modifications to the processes or procedures surveyed.

Should you have any questions regarding this report, please do not hesitate to contact me at (860) 549-7495.

Sincerely,


ATLAS TECHNICAL CONSULTANTS LLC



Douglas J. Rhoads, CHMM
Practice Team Manager

APPENDIX A

SAMPLE LOCATION DRAWING

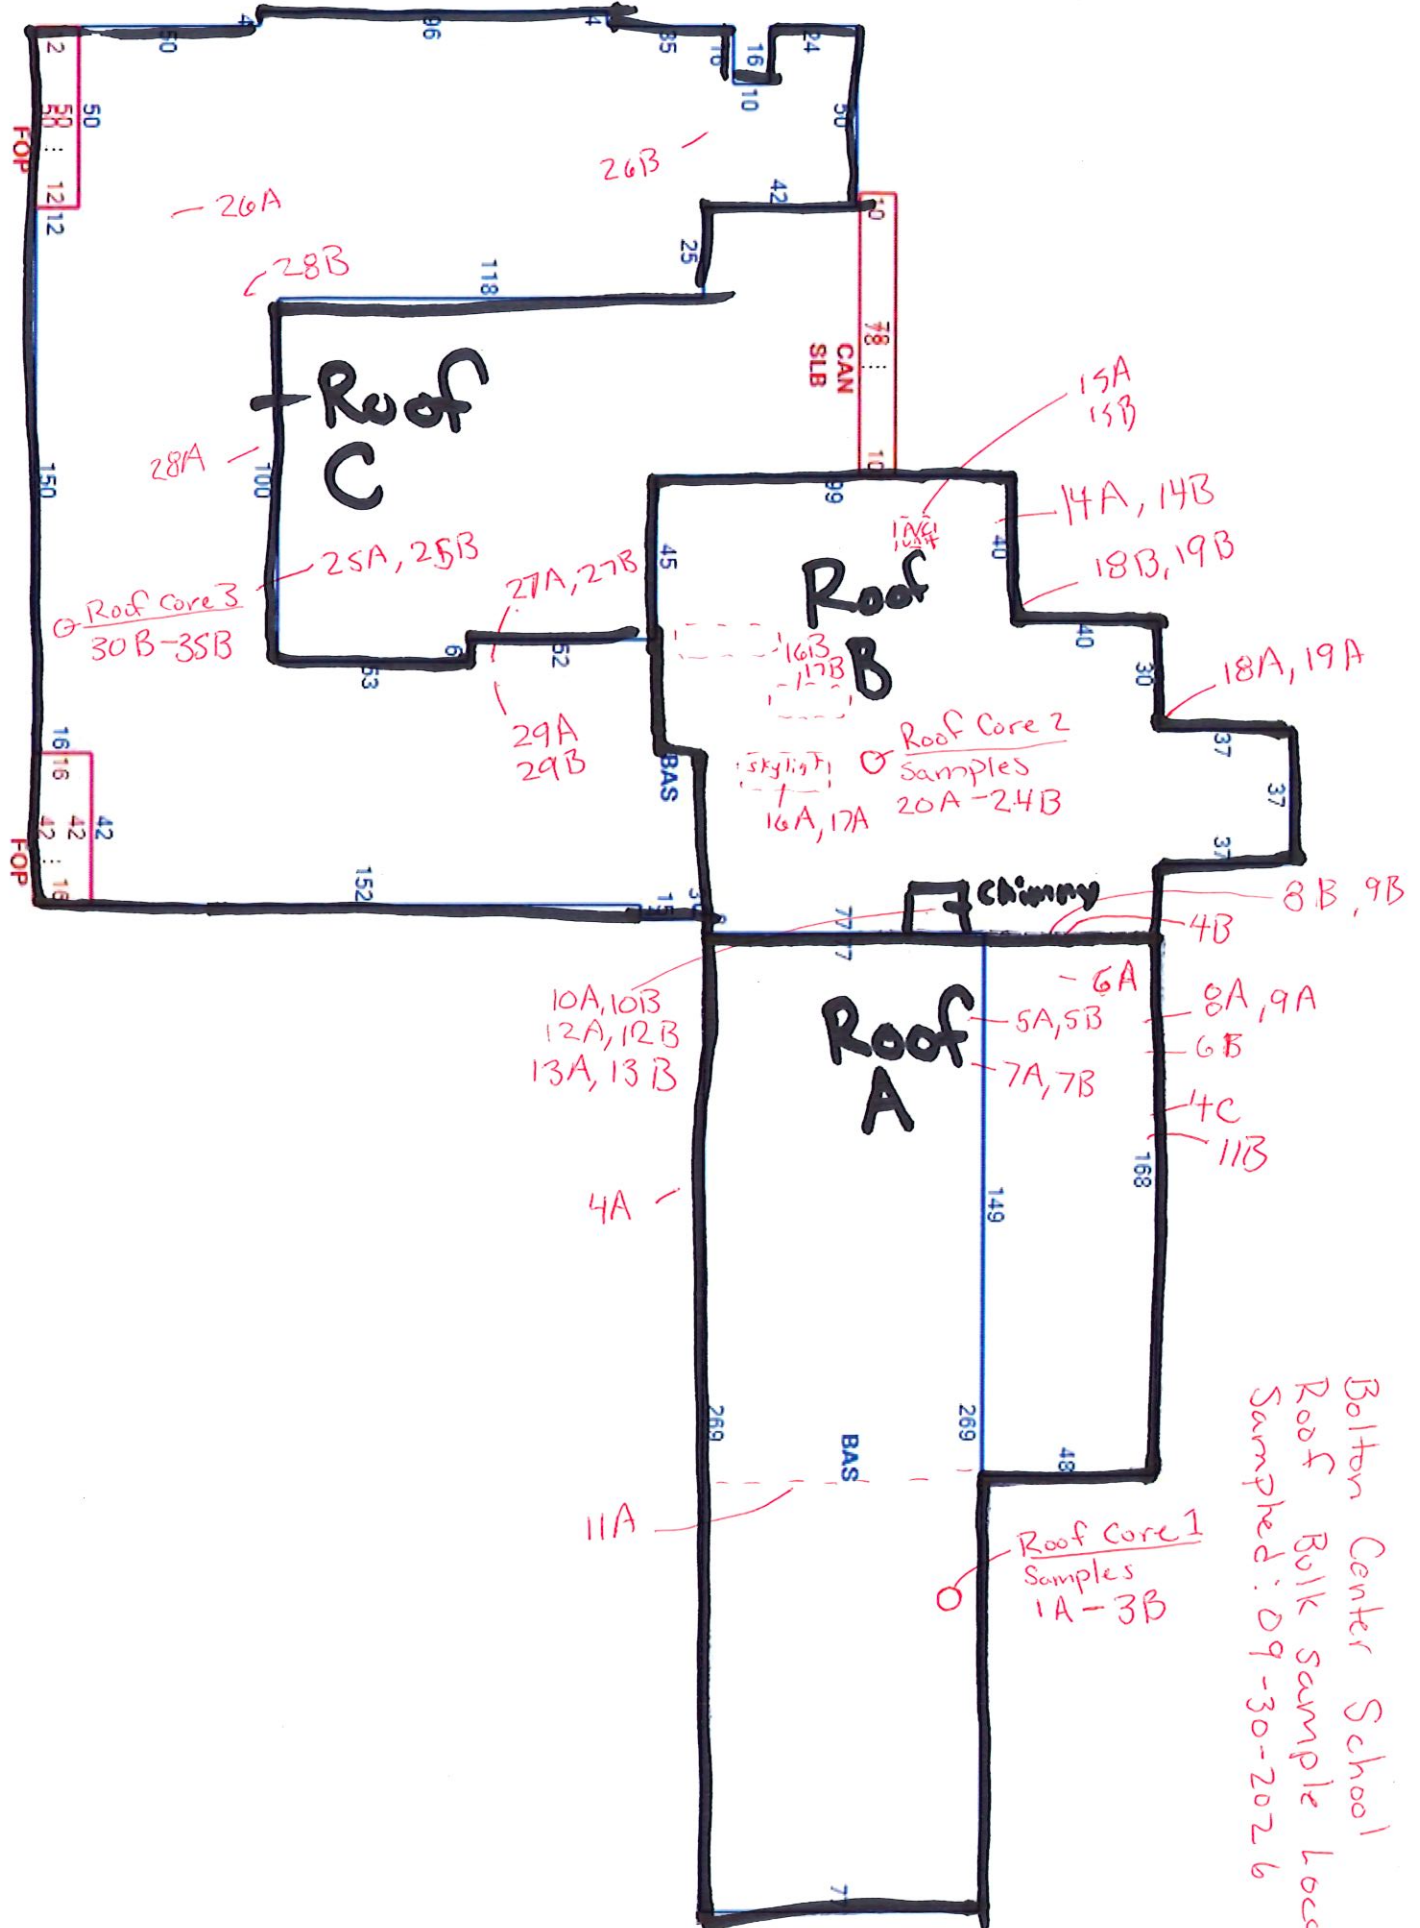

APPENDIX B

ASBESTOS SAMPLE RESULTS AND CHAIN OF CUSTODY



EMSL Analytical, Inc.

165 Gracey Avenue Meriden, CT 06451

Tel/Fax: (203) 284-5948 / (203) 284-5978

<http://www.EMSL.com> / meridenlab@emsl.com

EMSL Order: 242606070

Customer ID: ATCE54

Customer PO: 19-10133-0001

Project ID:

Attention: Doug Rhoads

Atlas Technical

290 Roberts Street

Suite 301

East Hartford, CT 06108

Phone: (860) 549-7495

Fax: (860) 282-9826

Received Date: 09/30/2026 3:50 PM

Analysis Date: 10/02/2026 - 10/05/2026

Collected Date: 09/30/2026

Project: 2438026001 / BOLTON CENTER SCHOOL, 108 NOTCH RD, BOLTON, CT 06043

Test Report: Asbestos Analysis of Bulk Materials via AHERA Method 40CFR 763 Subpart E Appendix E supplemented with EPA 600/R-93/116 using Polarized Light Microscopy

Sample	Description	Appearance	Non-Asbestos		Asbestos
			% Fibrous	% Non-Fibrous	% Type
093026-1A 242606070-0001	ROOF A CORE 1 - TOP TAR LAYER	Black Fibrous Heterogeneous	5% Glass	95% Non-fibrous (Other)	None Detected
093026-1B 242606070-0002	ROOF A CORE 1 - TOP TAR LAYER	Black Fibrous Heterogeneous	1% Cellulose 5% Glass	94% Non-fibrous (Other)	None Detected
093026-2A 242606070-0003	ROOF A CORE 1 - MIDDLE FIBROUS LAYER	Yellow Fibrous Homogeneous	98% Glass	2% Non-fibrous (Other)	None Detected
093026-2B 242606070-0004	ROOF A CORE 1 - MIDDLE FIBROUS LAYER	Yellow Fibrous Homogeneous	100% Glass		None Detected
093026-3A 242606070-0005	ROOF A CORE 1 - BOTTOM FOAM LAYER	Tan Non-Fibrous Homogeneous		100% Non-fibrous (Other)	None Detected
093026-3B 242606070-0006	ROOF A CORE 1 - BOTTOM FOAM LAYER	Yellow Non-Fibrous Homogeneous		100% Non-fibrous (Other)	None Detected
093026-4A 242606070-0007	ROOF A NORTH - STUCCO WALL	Gray/Tan Non-Fibrous Heterogeneous	2% Fibrous (Other)	35% Quartz 10% Ca Carbonate 53% Non-fibrous (Other)	None Detected
093026-4B 242606070-0008	ROOF A EAST - STUCCO WALL	Gray Non-Fibrous Heterogeneous		35% Quartz 10% Ca Carbonate 55% Non-fibrous (Other)	None Detected
093026-4C 242606070-0009	ROOF A SOUTH - STUCCO WALL	Gray/Black/Beige Non-Fibrous Heterogeneous	<1% Cellulose 1% Fibrous (Other)	45% Quartz 10% Ca Carbonate 44% Non-fibrous (Other)	None Detected
093026-5A 242606070-0010	ROOF A - WHITE VENT CAULKING	White Non-Fibrous Homogeneous		10% Ca Carbonate 90% Non-fibrous (Other)	None Detected
093026-5B 242606070-0011	ROOF A - WHITE VENT CAULKING	White Non-Fibrous Homogeneous		10% Ca Carbonate 90% Non-fibrous (Other)	None Detected
093026-6A 242606070-0012	ROOF A - BLACK ROOF PATCH	Black Fibrous Heterogeneous		92% Non-fibrous (Other)	8% Chrysotile
093026-6B 242606070-0013	ROOF A - BLACK ROOF PATCH	Black Non-Fibrous Homogeneous	<1% Cellulose	100% Non-fibrous (Other)	None Detected
093026-7A 242606070-0014	ROOF A - SILVER ROOF PATCH	Silver Non-Fibrous Homogeneous	<1% Cellulose	100% Non-fibrous (Other)	None Detected
093026-7B 242606070-0015	ROOF A - SILVER ROOF PATCH	Silver Non-Fibrous Heterogeneous	3% Cellulose	97% Non-fibrous (Other)	None Detected
093026-8A 242606070-0016	ROOF A - WHITE CAULKING ON FLASHING TAPE	White Non-Fibrous Homogeneous		10% Ca Carbonate 90% Non-fibrous (Other)	None Detected

Initial report from: 10/05/2026 14:51:42



EMSL Analytical, Inc.

165 Gracey Avenue Meriden, CT 06451

Tel/Fax: (203) 284-5948 / (203) 284-5978

<http://www.EMSL.com> / meridenlab@emsl.com

EMSL Order: 242606070

Customer ID: ATCE54

Customer PO: 19-10133-0001

Project ID:

Test Report: Asbestos Analysis of Bulk Materials via AHERA Method 40CFR 763 Subpart E Appendix E supplemented with EPA 600/R-93/116 using Polarized Light Microscopy

Sample	Description	Appearance	Non-Asbestos		Asbestos
			% Fibrous	% Non-Fibrous	% Type
093026-8B 242606070-0017	ROOF A - WHITE CAULKING ON FLASHING TAPE	Gray/White Fibrous Heterogeneous	2% Cellulose	10% Ca Carbonate 88% Non-fibrous (Other)	None Detected
093026-9A 242606070-0018	ROOF A - WHITE SEAM CAULKING	Gray/Black Non-Fibrous Homogeneous		10% Ca Carbonate 90% Non-fibrous (Other)	None Detected
093026-9B 242606070-0019	ROOF A - WHITE SEAM CAULKING	Gray/Silver Non-Fibrous Heterogeneous	<1% Cellulose <1% Synthetic	10% Ca Carbonate 90% Non-fibrous (Other)	None Detected
093026-10A 242606070-0020	ROOF A - CEMENT CHIMNEY CAP	Gray/Tan Non-Fibrous Heterogeneous		35% Quartz 10% Ca Carbonate 55% Non-fibrous (Other)	None Detected
093026-10B 242606070-0021	ROOF A - CEMENT CHIMNEY CAP	Gray/White Non-Fibrous Heterogeneous	<1% Cellulose	45% Quartz 10% Ca Carbonate 45% Non-fibrous (Other)	None Detected
093026-11A 242606070-0022	ROOF A - SHINGLE EDGE	Gray/Black Fibrous Heterogeneous	5% Synthetic	95% Non-fibrous (Other)	None Detected
093026-11B 242606070-0023	ROOF A - SHINGLE EDGE	Brown/Gray/Black Fibrous Heterogeneous	1% Cellulose 5% Synthetic	94% Non-fibrous (Other)	None Detected
093026-12A 242606070-0024	ROOF B - CHIMNEY BRICK	Red Non-Fibrous Homogeneous	<1% Cellulose	100% Non-fibrous (Other)	None Detected
093026-12B 242606070-0025	ROOF B - CHIMNEY BRICK	Brown/Orange Non-Fibrous Homogeneous		3% Quartz 97% Non-fibrous (Other)	None Detected
093026-13A 242606070-0026	ROOF B - CHIMNEY MORTAR	Gray Non-Fibrous Heterogeneous		35% Quartz 10% Ca Carbonate 55% Non-fibrous (Other)	None Detected
093026-13B 242606070-0027	ROOF B - CHIMNEY MORTAR	Gray/Tan/Beige Non-Fibrous Heterogeneous	<1% Cellulose <1% Glass	45% Quartz 10% Ca Carbonate 45% Non-fibrous (Other)	None Detected
093026-14A 242606070-0028	ROOF B - EDGE ROOF PATCH	Black/Silver Fibrous Heterogeneous	2% Cellulose	98% Non-fibrous (Other)	None Detected
093026-14B 242606070-0029	ROOF B - EDGE ROOF PATCH	Black/Silver Non-Fibrous Heterogeneous	3% Cellulose <1% Glass	97% Non-fibrous (Other)	None Detected
093026-15A 242606070-0030	ROOF B - AIR CONDITIONER UNIT PATCH	Black Non-Fibrous Homogeneous		10% Ca Carbonate 90% Non-fibrous (Other)	None Detected
093026-15B 242606070-0031	ROOF B - AIR CONDITIONER UNIT PATCH	Black Non-Fibrous Homogeneous	<1% Cellulose	100% Non-fibrous (Other)	None Detected
093026-16A 242606070-0032	ROOF B - SKYLIGHT SHINGLES	Black Fibrous Heterogeneous	20% Synthetic	80% Non-fibrous (Other)	None Detected
093026-16B 242606070-0033	ROOF B - SKYLIGHT SHINGLES	Brown/Black/Orange Non-Fibrous Heterogeneous	<1% Cellulose	100% Non-fibrous (Other)	None Detected
093026-17A 242606070-0034	ROOF B - SKYLIGHT CAULKING	Black Fibrous Heterogeneous	20% Cellulose	80% Non-fibrous (Other)	None Detected
093026-17B 242606070-0035	ROOF B - SKYLIGHT CAULKING	Gray/Black/Clear Non-Fibrous Heterogeneous	<1% Cellulose <1% Synthetic	100% Non-fibrous (Other)	None Detected

Initial report from: 10/05/2026 14:51:42



EMSL Analytical, Inc.

165 Gracey Avenue Meriden, CT 06451

Tel/Fax: (203) 284-5948 / (203) 284-5978

<http://www.EMSL.com> / meridenlab@emsl.com

EMSL Order: 242606070

Customer ID: ATCE54

Customer PO: 19-10133-0001

Project ID:

Test Report: Asbestos Analysis of Bulk Materials via AHERA Method 40CFR 763 Subpart E Appendix E supplemented with EPA 600/R-93/116 using Polarized Light Microscopy

Sample	Description	Appearance	Non-Asbestos		Asbestos
			% Fibrous	% Non-Fibrous	% Type
093026-18A 242606070-0036	ROOF B - WHITE FLASHING TAR	Tan Non-Fibrous Homogeneous		10% Ca Carbonate 90% Non-fibrous (Other)	None Detected
093026-18B 242606070-0037	ROOF B - WHITE FLASHING TAR	Tan/White/Black Non-Fibrous Heterogeneous	2% Cellulose	10% Ca Carbonate 88% Non-fibrous (Other)	None Detected
093026-19A 242606070-0038	ROOF B - BLACK FLASHING TAR	Black Fibrous Heterogeneous	5% Cellulose	95% Non-fibrous (Other)	None Detected
093026-19B 242606070-0039	ROOF B - BLACK FLASHING TAR	Tan/Black Fibrous Heterogeneous	5% Cellulose	95% Non-fibrous (Other)	None Detected
093026-20A 242606070-0040	ROOF B CORE 2 - TOP TAR LAYER	Black Fibrous Heterogeneous	5% Glass	95% Non-fibrous (Other)	None Detected
093026-20B 242606070-0041	ROOF B - TOP TAR LAYER	Black Fibrous Heterogeneous	<1% Cellulose 8% Glass	92% Non-fibrous (Other)	None Detected
093026-21A 242606070-0042	ROOF B - 2ND FIBROUS LAYER	Yellow Fibrous Homogeneous	99% Glass	1% Non-fibrous (Other)	None Detected
093026-21B 242606070-0043	ROOF B - 2ND FIBROUS LAYER	Yellow Fibrous Homogeneous	100% Glass		None Detected
093026-22A 242606070-0044	ROOF B - 3RD PAPER LAYER	Black Fibrous Heterogeneous	5% Glass	95% Non-fibrous (Other)	None Detected
093026-22B 242606070-0045	ROOF B - 3RD PAPER LAYER	Black/Yellow Fibrous Heterogeneous	1% Cellulose 30% Glass	69% Non-fibrous (Other)	None Detected
093026-23A 242606070-0046	ROOF B - 4TH FOAM LAYER	Tan Non-Fibrous Homogeneous		100% Non-fibrous (Other)	None Detected
093026-23B 242606070-0047	ROOF B - 4TH FOAM LAYER	White/Black/Yellow Non-Fibrous Heterogeneous	<1% Cellulose	100% Non-fibrous (Other)	None Detected
093026-24A 242606070-0048	ROOF B CORE 2 - BOTTOM PAPER LAYER	Brown/Gray Fibrous Heterogeneous	70% Cellulose	30% Non-fibrous (Other)	None Detected
093026-24B 242606070-0049	ROOF B CORE 2 - BOTTOM PAPER LAYER	Brown/Gray/Yellow Fibrous Heterogeneous	85% Cellulose 1% Glass	14% Non-fibrous (Other)	None Detected
093026-25A 242606070-0050	ROOF C - EDGE ROOF CAULKING	Gray Non-Fibrous Homogeneous		5% Ca Carbonate 95% Non-fibrous (Other)	None Detected
093026-25B 242606070-0051	ROOF C - EDGE ROOF CAULKING	Gray/Silver/Beige Non-Fibrous Heterogeneous	<1% Cellulose	100% Non-fibrous (Other)	None Detected
093026-26A 242606070-0052	ROOF C - BLACK VENT CAULKING	Black Fibrous Heterogeneous	10% Cellulose	90% Non-fibrous (Other)	None Detected
093026-26B 242606070-0053	ROOF C - BLACK VENT CAULKING	Brown/Black Fibrous Heterogeneous	5% Cellulose 1% Glass	94% Non-fibrous (Other)	None Detected
093026-27A 242606070-0054	ROOF C - RED SHINGLE	Black Fibrous Heterogeneous	10% Synthetic	90% Non-fibrous (Other)	None Detected

Initial report from: 10/05/2026 14:51:42



EMSL Analytical, Inc.

165 Gracey Avenue Meriden, CT 06451

Tel/Fax: (203) 284-5948 / (203) 284-5978

<http://www.EMSL.com> / meridenlab@emsl.com

EMSL Order: 242606070

Customer ID: ATCE54

Customer PO: 19-10133-0001

Project ID:

Test Report: Asbestos Analysis of Bulk Materials via AHERA Method 40CFR 763 Subpart E Appendix E supplemented with EPA 600/R-93/116 using Polarized Light Microscopy

Sample	Description	Appearance	Non-Asbestos		Asbestos
			% Fibrous	% Non-Fibrous	% Type
093026-27B 242606070-0055	ROOF C - RED SHINGLE	Brown/Black Fibrous Heterogeneous	5% Cellulose 1% Synthetic	94% Non-fibrous (Other)	None Detected
093026-28A 242606070-0056	ROOF C - EDGE ROOF PATCH	Black Fibrous Homogeneous	20% Cellulose	80% Non-fibrous (Other)	None Detected
093026-28B 242606070-0057	ROOF C - EDGE ROOF PATCH	Brown/Black Non-Fibrous Heterogeneous	3% Cellulose	97% Non-fibrous (Other)	None Detected
093026-29A 242606070-0058	ROOF C - SHINGLE SEAM CAULKING	Black Fibrous Heterogeneous	20% Cellulose	80% Non-fibrous (Other)	None Detected
093026-29B 242606070-0059	ROOF C - SHINGLE SEAM CAULKING	Brown/Gray/Black Fibrous Heterogeneous	8% Cellulose	92% Non-fibrous (Other)	None Detected
093026-30A 242606070-0060	ROOF C CORE 3 - TOP TAR LAYER	Black Fibrous Heterogeneous	10% Glass	90% Non-fibrous (Other)	None Detected
093026-30B 242606070-0061	ROOF C CORE 3 - TOP TAR LAYER	Brown/Black Fibrous Heterogeneous	1% Cellulose 5% Glass	94% Non-fibrous (Other)	None Detected
093026-31A 242606070-0062	ROOF C CORE 3 - 2ND FIBROUS LAYER	Tan Fibrous Homogeneous	97% Cellulose	3% Non-fibrous (Other)	None Detected
093026-31B 242606070-0063	ROOF C CORE 3 - 2ND FIBROUS LAYER	Brown/Black Fibrous Heterogeneous	99% Cellulose	1% Non-fibrous (Other)	None Detected
093026-32A 242606070-0064	ROOF C CORE 3 - 3RD PAPER LAYER	Tan/Black Fibrous Heterogeneous	30% Cellulose	70% Non-fibrous (Other)	None Detected
093026-32B 242606070-0065	ROOF C CORE 3 - 3RD PAPER LAYER	Brown/Gray/Black Fibrous Heterogeneous	95% Cellulose 2% Glass	3% Non-fibrous (Other)	None Detected
093026-33A 242606070-0066	ROOF C CORE 3 - 4TH FOAM LAYER	Tan/White Non-Fibrous Homogeneous	<1% Cellulose	100% Non-fibrous (Other)	None Detected
093026-33B 242606070-0067	ROOF C CORE 3 - 4TH FOAM LAYER	Tan/Yellow Non-Fibrous Heterogeneous	3% Cellulose	97% Non-fibrous (Other)	None Detected
093026-34A 242606070-0068	ROOF C CORE 3 - 5TH PAPER LAYER	Gray Fibrous Homogeneous	60% Cellulose 2% Glass	38% Non-fibrous (Other)	None Detected
093026-34B 242606070-0069	ROOF C CORE 3 - 5TH PAPER LAYER	Brown/Black/Yellow Fibrous Heterogeneous	65% Cellulose 1% Glass	34% Non-fibrous (Other)	None Detected
093026-35A 242606070-0070	ROOF C CORE 3 - 6TH FOAM LAYER	Tan Non-Fibrous Homogeneous	<1% Cellulose	100% Non-fibrous (Other)	None Detected
093026-35B 242606070-0071	ROOF C CORE 3 - 6TH FOAM LAYER	Yellow Non-Fibrous Homogeneous		100% Non-fibrous (Other)	None Detected



EMSL Analytical, Inc.

165 Gracey Avenue Meriden, CT 06451

Tel/Fax: (203) 284-5948 / (203) 284-5978

<http://www.EMSL.com> / meridenlab@emsl.com

EMSL Order: 242606070

Customer ID: ATCE54

Customer PO: 19-10133-0001

Project ID:

Analyst(s)

Cameron Evans (36)

Scott Combs (35)

Danny Sandhu, Asbestos Laboratory Manager
or Other Approved Signatory

EMSL maintains liability limited to cost of analysis. Interpretation and use of test results are the responsibility of the client. This report relates only to the samples reported above, and may not be reproduced, except in full, without written approval by EMSL. EMSL bears no responsibility for sample collection activities or analytical method limitations. The report reflects the samples as received. Results are generated from the field sampling data (sampling volumes and areas, locations, etc.) provided by the client on the Chain of Custody. Samples are within quality control criteria and met method specifications unless otherwise noted. The above analyses were performed in general compliance with Appendix E to Subpart E of 40 CFR (previously EPA 600/M4-82-020 "Interim Method") but augmented with procedures outlined in the 1993 ("final") version of the method. This report must not be used by the client to claim product certification, approval, or endorsement by NVLAP, NIST or any agency of the federal government. Non-friable organically bound materials present a problem matrix and therefore EMSL recommends gravimetric reduction prior to analysis. Unless requested by the client, building materials manufactured with multiple layers (i.e. linoleum, wallboard, etc.) are reported as a single sample. Estimation of uncertainty is available on request.

Samples analyzed by EMSL Analytical, Inc. Kernersville, NC NVLAP Lab Code 102104-0, Virginia 3333-000228, West Virginia LT000321

Initial report from: 10/05/2026 14:51:42

ATLAS

242606070

BULK SAMPLE LOG

Page 1 of 5

55 Hartland Street, Suite 100
East Hartford, CT 06108
(860) 282-9924

Atlas Inspector: Aaron Blanchflower		Client Name: Bolton Schools					
Accreditation No.: 1253		Project No./Task No.: 2438026001					
Survey Date: 9/30/2026		Project Manager: Doug Rhoads					
Signature: <i>Aaron Blanchflower</i>		Requested Completion Date: <i>9/30/2026</i>					
Lab Name: EMSL	Requested turnaround time (circle)	3 HR	6 HR				
		24 HR	48 HR				
		3 DY	5 DY				
No. Samples Collected <u>71</u>							
Building: Bolton Center School							
Address: 108 Notch Rd, Bolton, CT 06043							
Sample Location	Material Description	Type S TSI MISC	Estimated Quantity	Friable Y/N	Condition (SD D ND)	Sample of _ (homogeneous material)	Field Number
Roof A core 1	Top tar layer	MISC				1	093026-1A
Roof A core 1						2	093026-1B
Roof A core 1	Middle fibrous layer	MISC				1	093026-2A
Roof A core 1						2	093026-2B
Roof A core 1	Bottom Foam layer	MISC				1	093026-3A
Roof A core 1						2	093026-3B
Roof A North	Stucco wall	MISC				1	093026-4A
Roof A East						2	093026-4B
Roof A South	Stucco wall	MISC				3	093026-4C
Roof A	White vent caulking	MISC				1	093026-5A
Roof A						2	093026-5B
Roof A	Black roof patch	MISC				1	093026-6A
Roof A						2	093026-6B
Roof A	Silver roof patch	MISC				1	093026-7A
Roof A						2	093026-7B
Type of Analysis (circle): PLM TEM Pt. Count PLM Qualitative							

Comments:

Damage Factors:
Disturbance Factors:

Physical (sig ding-ding-no ding)
Proximity (<1ft-1.5ft->6ft)

Ventilation (yes-no, if yes, type)

Relinquished By/Date:

Relinquished By/Date:

Notes

Water (extensive-moderate-slight-none)
Accessibility (within reach-barely
reachable-not reachable)

Air conduits (air plenum - air shaft -
elevator shaft - duct)

Aaron Blanchflower / *Aaron Blanchflower* 9-30-26

Deterioration (heavy-moderate-light-none)
Vibration (sym-music rm-auditorium-mechanical rm-elevator-other)


Air movement (high-moderate-low)

Received By/Date:

Received By/Date:

Etchability (yes-no) (mod-soft-rough)
Barrel (yes-no) (mod-soft-rough)

Texture (rough-pitted-moderate-smooth)



ATLAS

242606070

BULK SAMPLE LOGPage 2 of 5

55 Hardland Street, Suite 100
East Hartford, CT 06108
(860) 282-9924

Atlas Inspector: Aaron Blanchflower		Client Name: Bolton Schools	
Accreditation No.: 1253		Project No./Task No.: 2438026001	
Survey Date: 9/30/2026		Project Manager: Doug Rhoads	
Signature: <i>Aaron Blanchflower</i>		Requested Completion Date: _____	
Lab Name: EMSL	Requested turnaround time (circle)	3 HR	6 HR
		24 HR	48 HR
		3 DY	5 DY
Building: Bolton Center School			
Address: 108 Notch Rd, Bolton, CT 06043			

Sample Location	Material Description	Type S	Estimated Quantity	Friable Y/N	Condition (SD D ND)	Sample of homogeneous material	Field Number
Roof A	White caulking on flashing tape	MISC				1	093026-8A
Roof A						2	093026-8B
Roof A	White seam caulking	MISC				1	093026-9A
Roof A						2	093026-9B
Roof A	Cement Chimney cap	MISC				1	093026-10A
Roof A						2	093026-10B
Roof A	Shingle edge	MISC				1	093026-11A
Roof A						2	093026-11B
Roof B	Chimney brick	MISC				1	093026-12A
Roof B						2	093026-12B
Roof B	Chimney mortar	MISC				1	093026-13A
Roof B						2	093026-13B
Roof B	Edge roof patch	MISC				1	093026-14A
Roof B						2	093026-14B
Roof B	Air conditioner unit patch	MISC				1	093026-15A
Roof B						2	093026-15B

Type of Analysis (circle) : PLM TEM Pt. Count PLM Qualitative

Comments: RECEIVED SEP 30 2026

Damage Factors: _____

Disturbance Factors: _____

Relinquished By/Date: _____

Relinquished By/Date: _____

Notes: _____

Water (extensive-moderate-slight-none) _____

Accessibility (within reach-barely reachable-not reachable) _____

Air conduits (air plenum - air shaft - elevator shaft - duct) _____

Physical (sig dmg-dmg-no dmg) Proximity (<1ft- 1-5ft- >5ft) _____

Ventilation (yes-no; if yes, type) _____

Aaron Blanchflower *Aaron Blanchflower* 9-30-26

Relinquished By/Date: _____

Relinquished By/Date: _____

Deterioration (heavy-moderate-light-none) _____

Vibration (gym-music rm-auditorium-mechanical rm-elevator-other) _____

Air movement (high-moderate-low) _____

Texture (rough-pitted-moderate-smooth) _____

Friable By _____

Barriers (perm air/tit-enclosed-encapsulated) _____

ATLAS


242606070

BULK SAMPLE LOGPage 2 of 555 Hartland Street, Suite 100
East Hartford, CT 06108
(860) 282-9924

Atlas Inspector: Aaron Blanchflower		Client Name: Bolton Schools					
Accreditation No.: 1253		Project No./Task No.: 2438026001					
Survey Date: 9/30/2026		Project Manager: Doug Rhoads					
Signature: <i>[Signature]</i>							
Lab Name: EMSL		Requested Completion Date:					
Requested turnaround time (circle)		3 HR	6 HR				
		24 HR	48 HR				
		3 DY	5 DY				
Building: Bolton Center School							
Address: 108 Notch Rd, Bolton, CT 06043							
Sample Location	Material Description	Type S TSI MISC	Estimated Quantity	Friable Y/N	Condition (SD D ND)	Sample of homogeneous material)	Field Number
Roof B	Skylight shingles	MISC				1	093026-16A
Roof B						2	093026-16B
Roof B	Skylight caulking	MISC				1	093026-17A
Roof B						2	093026-17B
Roof B	White flashing tar	MISC				1	093026-18A
Roof B						2	093026-18B
Roof B	Black flashing tar	MISC				1	093026-19A
Roof B						2	093026-19B
Roof B Core 2	Top tar layer	MISC				1	093026-20A
Roof B						2	093026-20B
Roof B	2nd fibrous layer	MISC				1	093026-21A
Roof B						2	093026-21B
Roof B	3rd paper layer	MISC				1	093026-22A
Roof B						2	093026-22B
Roof B	4th foam layer	MISC				1	093026-23A
Roof B						2	093026-23B
Type of Analysis (circle): <u>PLM</u> <u>TEM</u> <u>BT</u> PLM Qualitative							

Comments:

Damage Factors:	Physical (sig dmg-dmg-no dmg)	Water (extensive-moderate-slight-none)	Notes
Disturbance Factors:	Proximity (<1ft- 1-6ft- >6ft)	Accessibility (within reach-barely reachable-not reachable)	Deterioration (heavy-moderate-light-none)
	Ventilation (yes-no; if yes, type)	Air conduits (air plenum - air shaft - riser for shaft - duct)	Vibration (gym-music rm-auditorium-mechanical rm-elevators and other)
			Air movement (high-moderate-low)
Relinquished By/Date:	Aaron Blanchflower	9-30-26	Received By/Date:
Relinquished By/Date:			Received By/Date:



ATLAS**BULK SAMPLE LOG**Page 4 of 555 Hartland Street, Suite 100
East Hartford, CT 06108
(860) 282-9924

Atlas Inspector: Aaron Blanchflower		Client Name: Bolton Schools					
Accreditation No.: 1253		Project No./Task No.: 2438026001					
Survey Date: 9/30/2026		Project Manager: Doug Rhoads					
Signature: <i>Aaron Blanchflower</i>							
Lab Name: EMSL		Requested Completion Date:					
Requested turnaround time (circle)		3 HR	6 HR 24 HR 48 HR 3 DY 5 DY				
Building: Bolton Center School							
Address: 108 Notch Rd, Bolton, CT 06043							
Sample Location	Material Description	Type S TSI MISC	Estimated Quantity	Friable Y/N	Condition (SD D ND)	Sample of _ (homogeneous material)	Field Number
Roof B core 2	Bottom paper layer	MISC				1	093026-24A
Roof B core 2						2	093026-24B
Roof C	Edge roof caulking	MISC				1	093026-25A
Roof C						2	093026-25B
Roof C	Black vent caulking	MISC				1	093026-26A
Roof C						2	093026-26B
Roof C	Red shingle	MISC				1	093026-27A
Roof C						2	093026-27B
Roof C	Edge roof patch	MISC				1	093026-28A
Roof C						2	093026-28B
Roof C	Shingle seam caulking	MISC				1	093026-29A
Roof C						2	093026-29B
Roof C core 3	Top tar layer	MISC				1	093026-30A
Roof C core 3						2	093026-30B
Roof C core 3	2nd fibrous layer	MISC				1	093026-31A
Roof C core 3						2	093026-31B

Type of Analysis (circle) : PLM TEM Pt. Count PLM Qualitative

Comments:

Damage Factors:
Disturbance Factors:Physical (sig ding-dmg-no dmg)
Proximity (<1ft- 1-5ft- >5ft)
Ventilation (yes-no, if yes, type)Water (extensive-moderate-slight-none)
Accessibility (within reach-barely reachable-not reachable)
Air conduits (air plenum - air shaft - elevator shaft - duct)Notes
Deterioration (heavy-moderate-light-none)
Vibration (gym-music rm-auditorium-mechanical rm-elevator-oh)

Texture (rough-pitted-moderate-smooth)

Relinquished By/Date:
Relinquished By/Date:Aaron Blanchflower *Aaron Blanchflower* 9-30-26Received By/Date:
Received By/Date:

55 Hartland Street, Suite 100
East Hartford, CT 06108
(860) 282-9924

Atlas Inspector: Aaron Blanchflower		Client Name: Bolton Schools						
Accreditation No.: 1253		Project No./Task No.: 2438026001						
Survey Date: 9/30/2026		Project Manager: Doug Rhoads						
Signature: <i>[Signature]</i>		Requested Completion Date: <i>[Signature]</i>						
Lab Name: EMSL	Requested turnaround time (circle)	3 HR	6 HR	24 HR	48 HR	3 DY	5 DY	No. Samples Collected
Building: Bolton Center School Address: 108 Notch Rd, Bolton, CT 06043								
Sample Location	Material Description	Type TSI MISC	Estimated Quantity	Friable Y/N	Condition (SD D ND)	Sample of _ (homogeneous material)	Field Number	
Roof C core 3	3 RD paper layer	MISC				1	093026- 32A	
Roof C core 3						2	093026- 32B	
Roof C core 3	4 th foam layer	MISC				1	093026- 33A	
Roof C core 3						2	093026- 33B	
Roof C core 3	5 th paper layer	MISC				1	093026- 34A	
Roof C core 3						2	093026- 34B	
Roof C core 3	6 th foam layer	MISC				1	093026- 35A	
Roof C core 3						2	093026- 35B	
Type of Analysis (circle) : PLM		TEM	Pt. Count	PLM Qualitative				
Comments: <i>[Signature]</i>								

By — Friability (yes-no; hard-modified-soft surface)
— Beadles (pearl-audight-enclosed-encapsulated)
Texture (rough-pitted-moderate-smooth)

Deterioration (heavy-moderate-light-none)
gym-music rm-auditorium-mechanical rm-ele

Vibration
Air movement (high-moderate-low)

Physical (sig dmng-dmg-no dmng)	Proximity (<1ft-16ft->8ft)	Water (extensive-moderate-slight-none)	Notes
Ventilation (yes-no; if yes, type)	Accessibility (within reach-barely reachable-not reachable)	Air conduits (air plenum - air shaft - elevator shaft-duct)	

Relinquished By/Date:
Relinquished By/Date:

Aaron Blanchflower / *[Signature]* 9-30-26
elevator shaft duct

Received By/Date:

APPENDIX C

INSPECTOR LICENSES

STATE OF CONNECTICUT
DEPARTMENT OF PUBLIC HEALTH

PURSUANT TO THE PROVISIONS OF THE GENERAL STATUTES OF CONNECTICUT

THE INDIVIDUAL NAMED BELOW IS CERTIFIED
BY THIS DEPARTMENT AS A
ASBESTOS CONSULTANT-INSPECTOR


ARLENE E BLACKWELL

CERTIFICATE NO.
001151

CURRENT THROUGH
07/31/27

VALIDATION NO.
03-290834


SIGNATURE


MANISHA JUTHANI, MD, COMMISSIONER



State of Connecticut

Lookup Detail View

Name

AARON M BLANCHFLOWER

License Information

lookup

License Type

Asbestos Consultant-Inspector

License Number

1253

Expiration Date

05/31/2027

Granted Date

05/07/2025

License Name

AARON BLANCHFLOWER

License Status

ACTIVE

CURRENT

Licensure Actions or Pending Charges

None

6/17/2026 10:52:27 AM
